

Los Alamos Hills Sports Park Soccer Field Synthetic Turf Renovation

Thursday, January 29, 2026

Project started 1/12 and project completed 1/29; two weeks ahead of schedule. Team access is OK for 1/30.




Alderwood Park
Pickleball Construction
Thursday, January 29, 2026

Construction fencing up, grading done, court fence posts in, concrete forms ready.



Alderwood Park
Pickleball Construction
Thursday, February 5, 2026
CONCRETE POUR

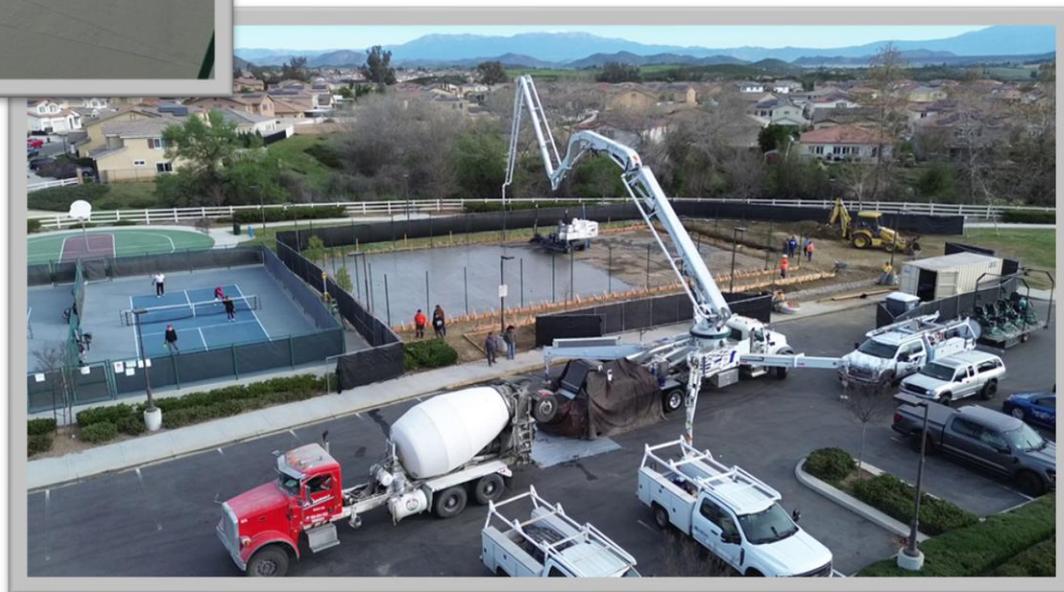

Alderwood Park Pickleball Construction Friday, February 6, 2026

Concrete poured, bioswale box underway, and drainage proceeding



Alderwood Park
Pickleball Construction
Friday, February 20, 2026

Concrete poured for access path, some plant material installed, bioswale box backfilling

