Received After Agenda Printed 03/19/2024 - Regular Meeting City Manager - Administrative Update



Update: Children's Library Expansion Project

Brian Crawford, Senior Program Manager March 19, 2024


Progress Recap


- June 2023: Design contract awarded to SVA
- July & August 2023: Stakeholder Visioning Workshops
- September November 2023: Refine Preliminary Design & Overall Budget
- January 2024: City Council confirms Expansion Project is a priority
- SVA is now working on schematic design and construction cost estimate



THE FOLLOWING SLIDES CONTAIN CONCEPTUAL DRAWINGS AND ARE SUBJECT TO CHANGE



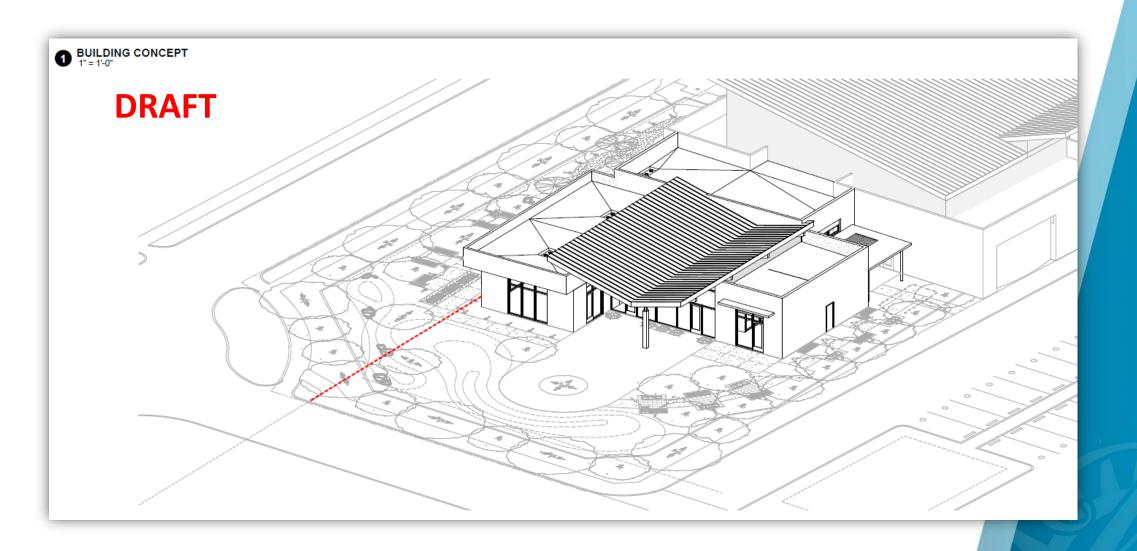

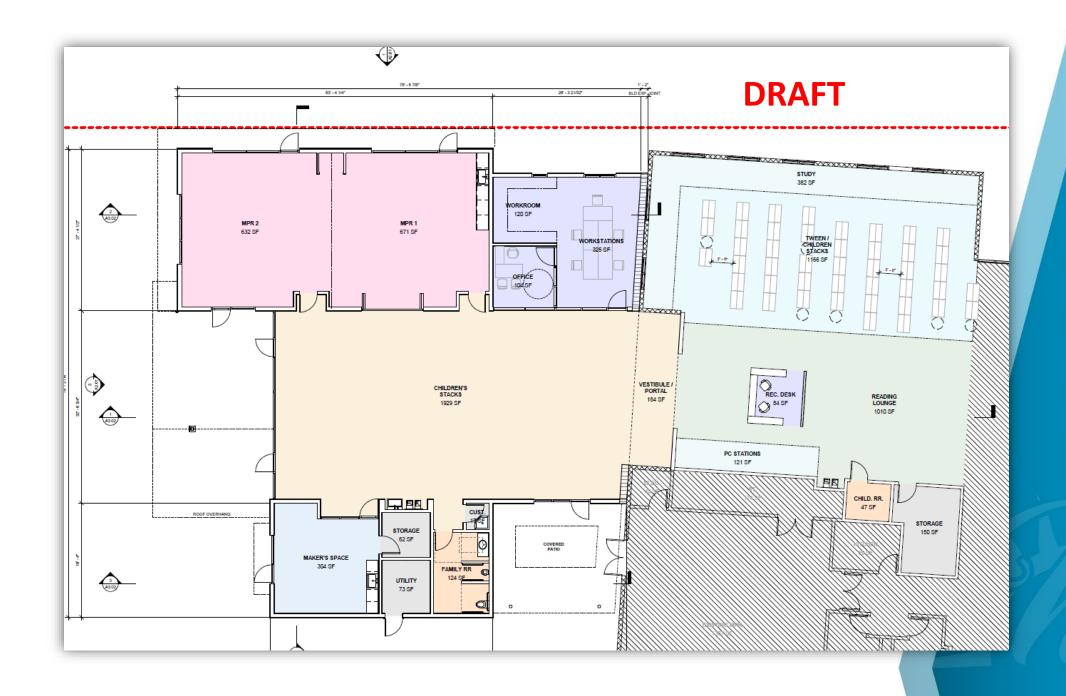


DRAFT

SD - PERSPECTIVE 01





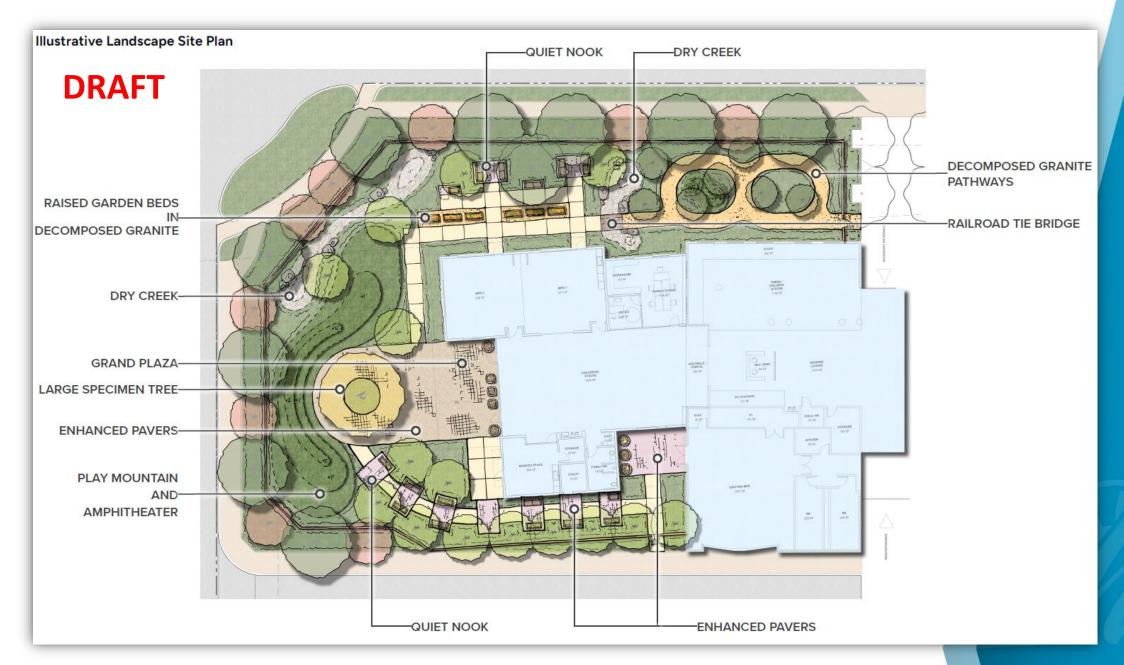

Next Steps

- April July 2024: Design Development
- July November 2024: Construction Documents & Plan Check
- November 2024 February 2025: Bidding & Contracts
- March 2025: Start of Construction



